



Arlington High School Building Project

AHS Construction Update – September 7th, 2023

Arlington HS Construction Schedule: April 2020 – September 2025

Construction Details

Phase 1 construction is complete and the new Performing Arts and Science, Technology, Engineering, Arts & Mathematics wings are open. Phase 2 began immediately after the Phase 1 building turnover. Part of the old school has been demolished and that area is closed off from the existing school during the next phase of construction.

COVID-19 Update


The health and safety of the community and workers on-site are of the highest priority and were taken into consideration in all project-related decisions. The Town of Arlington continues to monitor all state and federal guidelines regarding best practices during this unusual time and will modify recommendations as necessary to maintain safety and health for our community and construction workers.

Sign up for Weekly Construction Updates
<https://ahsbuilding.org/news/construction-updates/>
 For more information, visit:
www.ahsbuilding.org
 Email questions or concerns to:
ahsbuilding@arlington.k12.ma.us

For immediate, on-site assistance contact Hal Raymond, Skanska Site Representative,
 (617) 352-8593



PHASE 2 BUILDING CONSTRUCTION (February 2022 – October 2023)

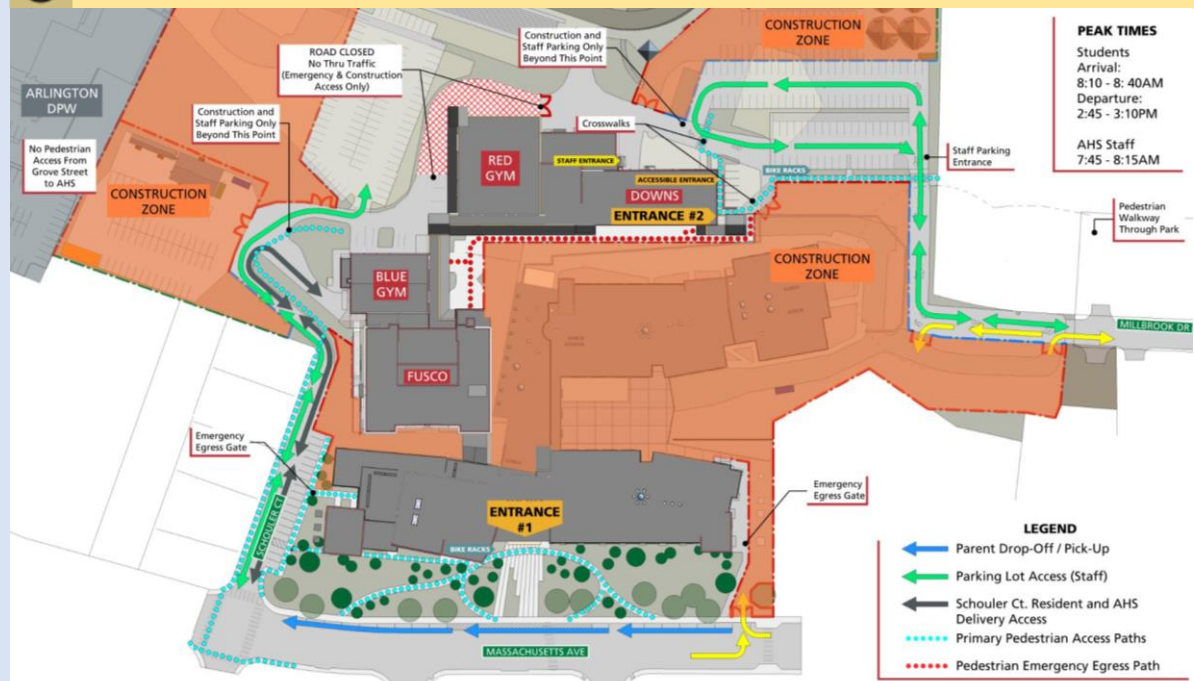

PEAK TIMES
 Students
 Arrival: 8:10 - 8:40AM
 Departure: 2:45 - 3:10PM
 AHS Staff
 7:45 - 8:15AM

Construction Look Ahead – Week of September 11th, 2023

The above diagram covers all work to be performed during the current phase. Specific work to be performed this week includes:

Public Way Impacts:

- Deliveries ongoing

General Site Activities:

- Phase 2:
 - Installation of masonry
 - Drywall installation, taping and sanding, and painting
 - Installation of marker boards, bathroom partitions, and accessories
 - Installation of ceiling grids and ceiling tiles
 - Installation of interior windows and casework
 - Install mechanical, electrical, telecommunication, plumbing, and fire sprinklers
 - Installation of plumbing and electrical fixtures
 - Start-up and testing of mechanical units
 - Grading of exterior site
 - Install of permanent Retaining Wall
- Material Stockpile/Temp Construction Lot for contractor storage and parking
- Schouler Court:
 - Construction vehicles entering and exiting project site.

Weekend Work/Holiday Work/Night Work:

- Saturday work is required for the foreseeable future.



Skanska USA Inc.
 Owner's Project Manager



Consigli Construction Co., Inc.
 Construction Manager at Risk



HMFH Architects, Inc.
 Architect

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF SEPTEMBER 11TH, 2023



Photograph 1: Library Progress



Photograph 2: Building B Elliptical Light Well Progress

ARLINGTON HIGH SCHOOL

WEEKLY UPDATE – WEEK OF SEPTEMBER 11TH, 2023



Photograph 3: Phase 2 North Elevation of Building B Entrance



Photograph 4: Phase 2 East Elevation (Mill Brook Dr)
